



plante moran | cresa

2021 Capital Bond Project Schedule



2022 – 2023 Construction Activities

June 14, 2022



Scope of Work by Series and Year

Series I Projects – Total Funding \$23.5M (\$17.5M Construction & Fees)


- Spring-Fall 2022
 - Beech Renovations
 - Keeler Renovations
 - Temporary Relocation of Central Office (north end)
 - MacGowan Swing Space 22/23 School Year
 - Transportation Parking Lot
 - Hilbert Track

Series II Projects - Total Funding \$35.8M (\$30M Construction & Fees)

- Fall 2022 – Winter 2023
 - RUHS Auto Shop / Auditorium Renovations
- Old Schoolhouse Exterior



Summer 2022 Construction Plan

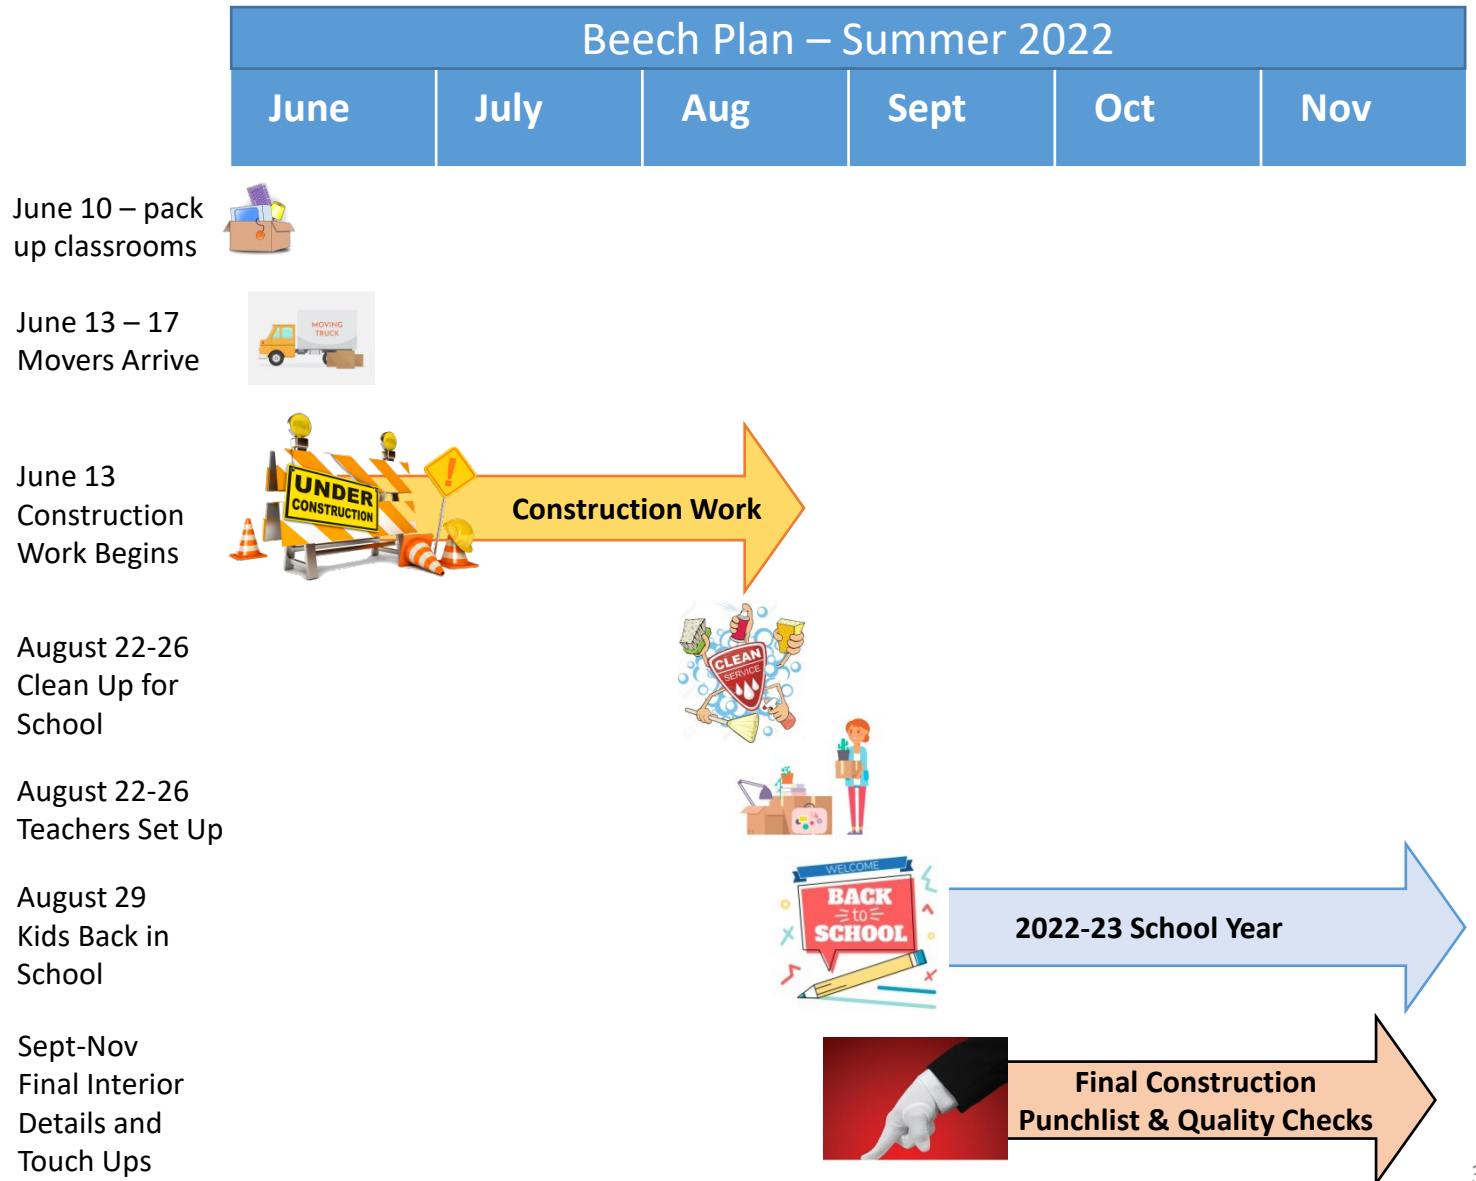



Summer 2022 Construction Plan

Keeler & MacGowan Plan – Summer 2022

June

July

Aug

Sept

Oct

Nov

June 10 – pack up MacGowan Relocate Central Office




June 13 Construction Work Begins At Keeler




August 22-26 Clean Up for School



August 15 – 19 Movers bring MacGowan to Keeler



August 22-26 Teachers Set Up @ Keeler



August 29 Kids Back in School



2022-23 School Year

Sept-Nov Final Interior Details and Touch Ups



Final Construction Punchlist & Quality Checks



2021 Capital Bond Project Update

Questions & Discussion
